


Tree Protection


This AMS should be read in conjunction with the Tree Protection Plan, as it cross-references the Tree Protection Plan for each specific area of work.

It is essential to adhere to the recommendations within this document during on-site operations to ensure the successful retention of trees as part of the proposed development. Compliance with the AMS will be a requirement of all relevant contracts associated with the proposed development.

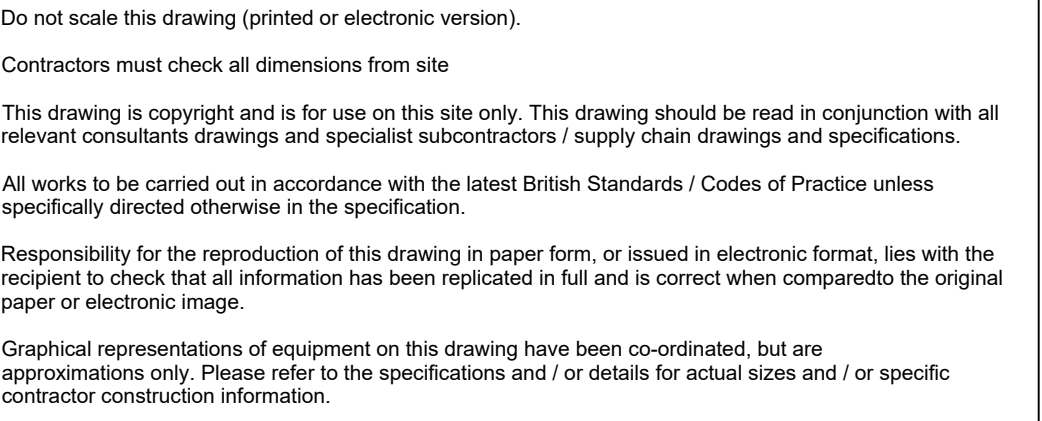

- | | |
|---|--|
|  | Category A tree, group or hedge |
|  | Category B tree, group or hedge |
|  | Category C tree, group or hedge |
|  | Category U tree, group or hedge |
|  | Retained tree |
|  | Root Protection Area (RPA) |
|  | Position estimated on site |
|  | Protective fencing (See Insert 1 & Insert 2) |
|  | Ground protection (See Insert 3) |

REV.	DATE	DESCRIPTION	DRAWN	CHK'D



T: +44 (0) 161 312 3131
weareurbangreen.co.uk

Client: **TAYLOR WIMPEY**


Project: **STANDEN FARM, PENDLE ROAD
CLITHEROE PHASE 2, 3 & 4**

Title: **ARBORICULTURAL
METHOD STATEMENT**

Issue: PLANNING

Drawn:	KO	Checked:	AB	Approved:	KO
Project:	UG132	Scale @ A0:	1:500	Date:	16/03/21
Dwg No:	UG_132_ARB_AMS_01			Revision:	00


Back-stay support

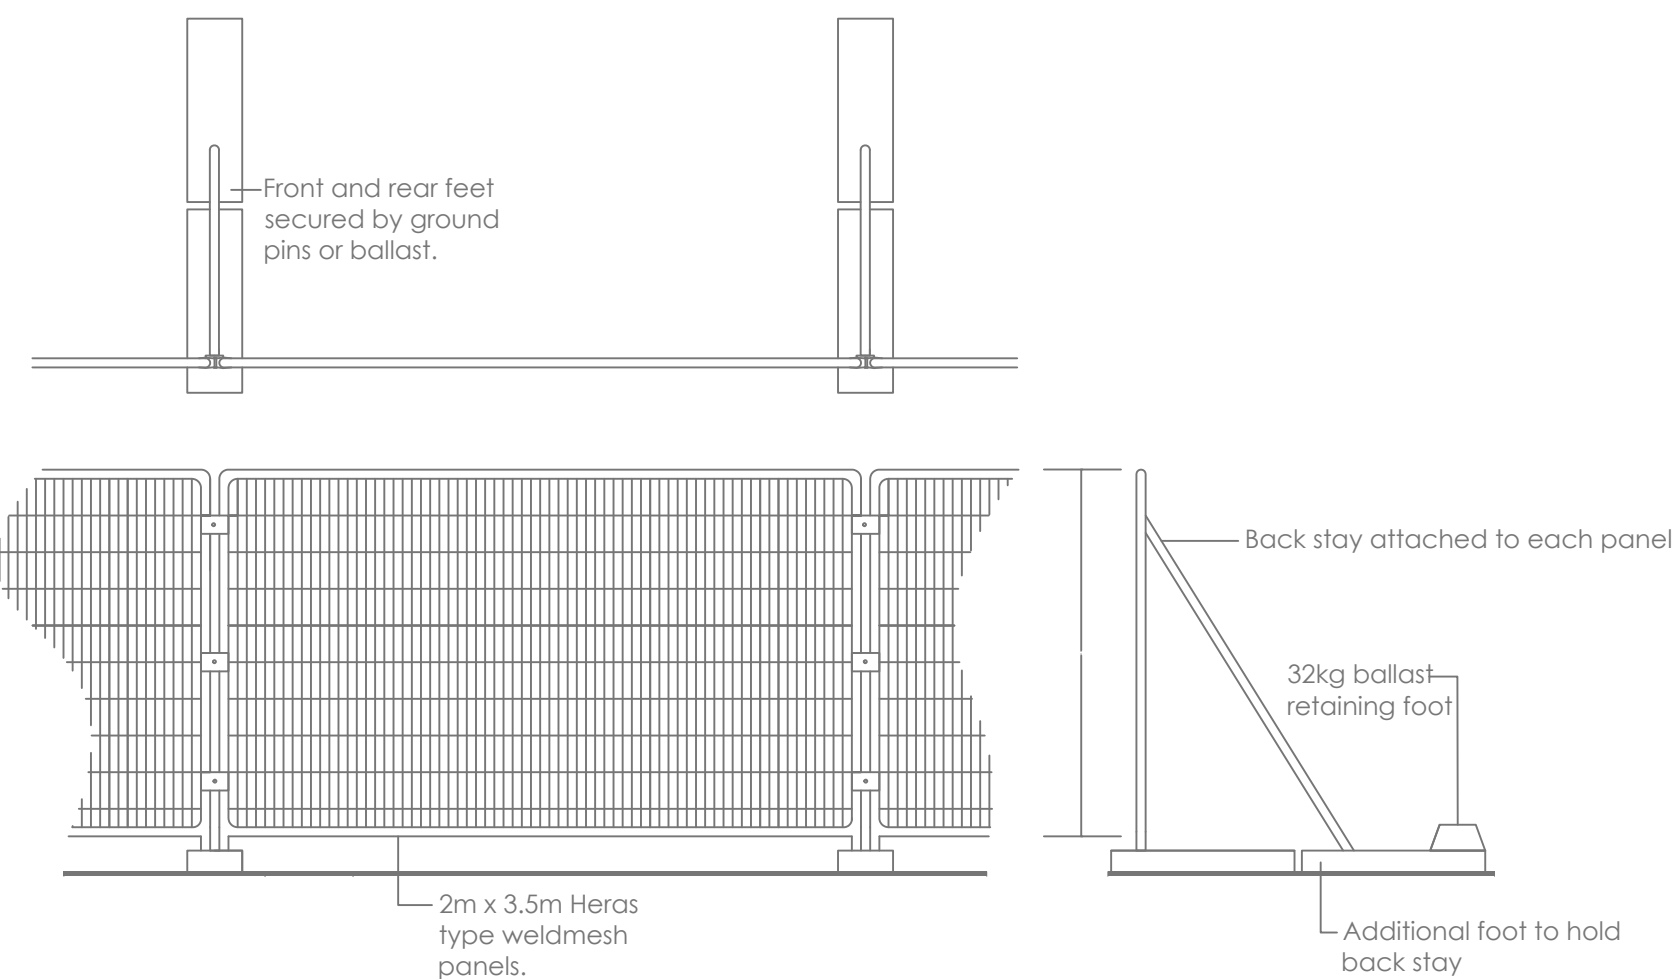

Insert 2: Tree protection notice




Insert 3: Ground protection specification

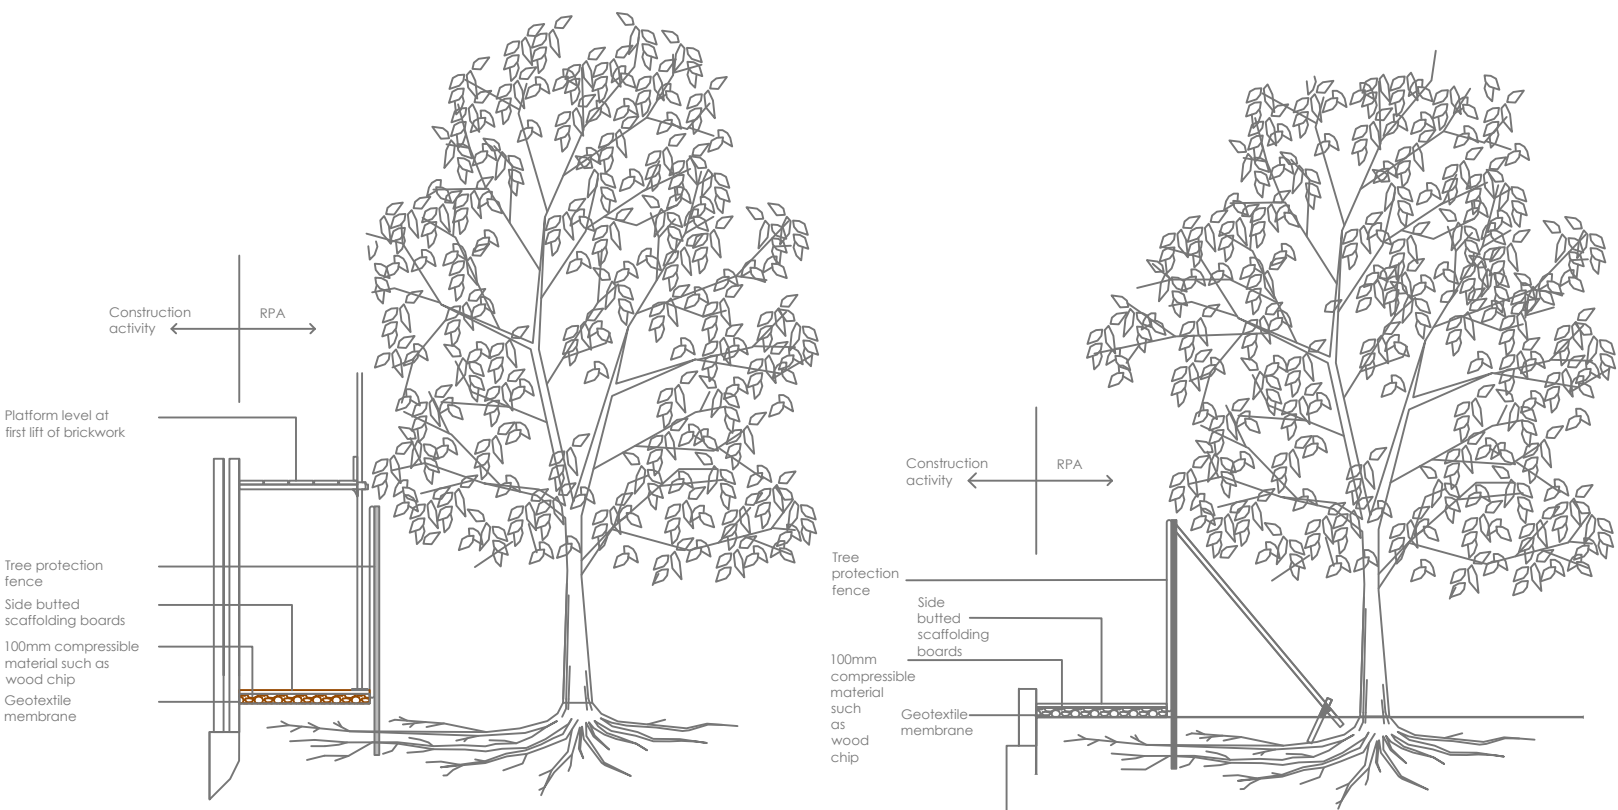

Arboricultural Method Statement (AMS)
Standen Farm, Pendle Road, Clitheroe,
Phase 2,3 and 4
Excavations and Root Pruning

1.
- Any necessary excavation must be carried out using hand tools to avoid direct damage to the protective bark of tree roots. It may be possible in some instances to use specialised equipment such as high air pressure machinery to excavate the soil with minimal disturbance to roots.
2.
- Exposed roots will be wrapped in dry, clean Hessian sacking to prevent desiccation and to protect from rapid temperature changes. In warmer weather, the sacking should be kept moist by regular watering. Sacking should be removed before backfilling.
3.
- Roots less than 25mm diameter may be pruned back, preferably to a growing point. A sharp cutting tool such as bypass secateurs or a handsaw should be used to leave the smallest wound possible. Roots greater than 25mm in diameter should be retained wherever possible.
4.
- Root pruning should be carried out under the supervision of the Arboricultural Consultant to ensure that only roots necessary to facilitate the development will be removed and the long-term well-being of retained trees is maintained.
5.
- Backfilling of any excavation should be carried out by hand to avoid direct root damage by excessive compaction and should include, where possible, the replacement of inert granular material mixed with sharp sand (not builder's sand) around retained roots.

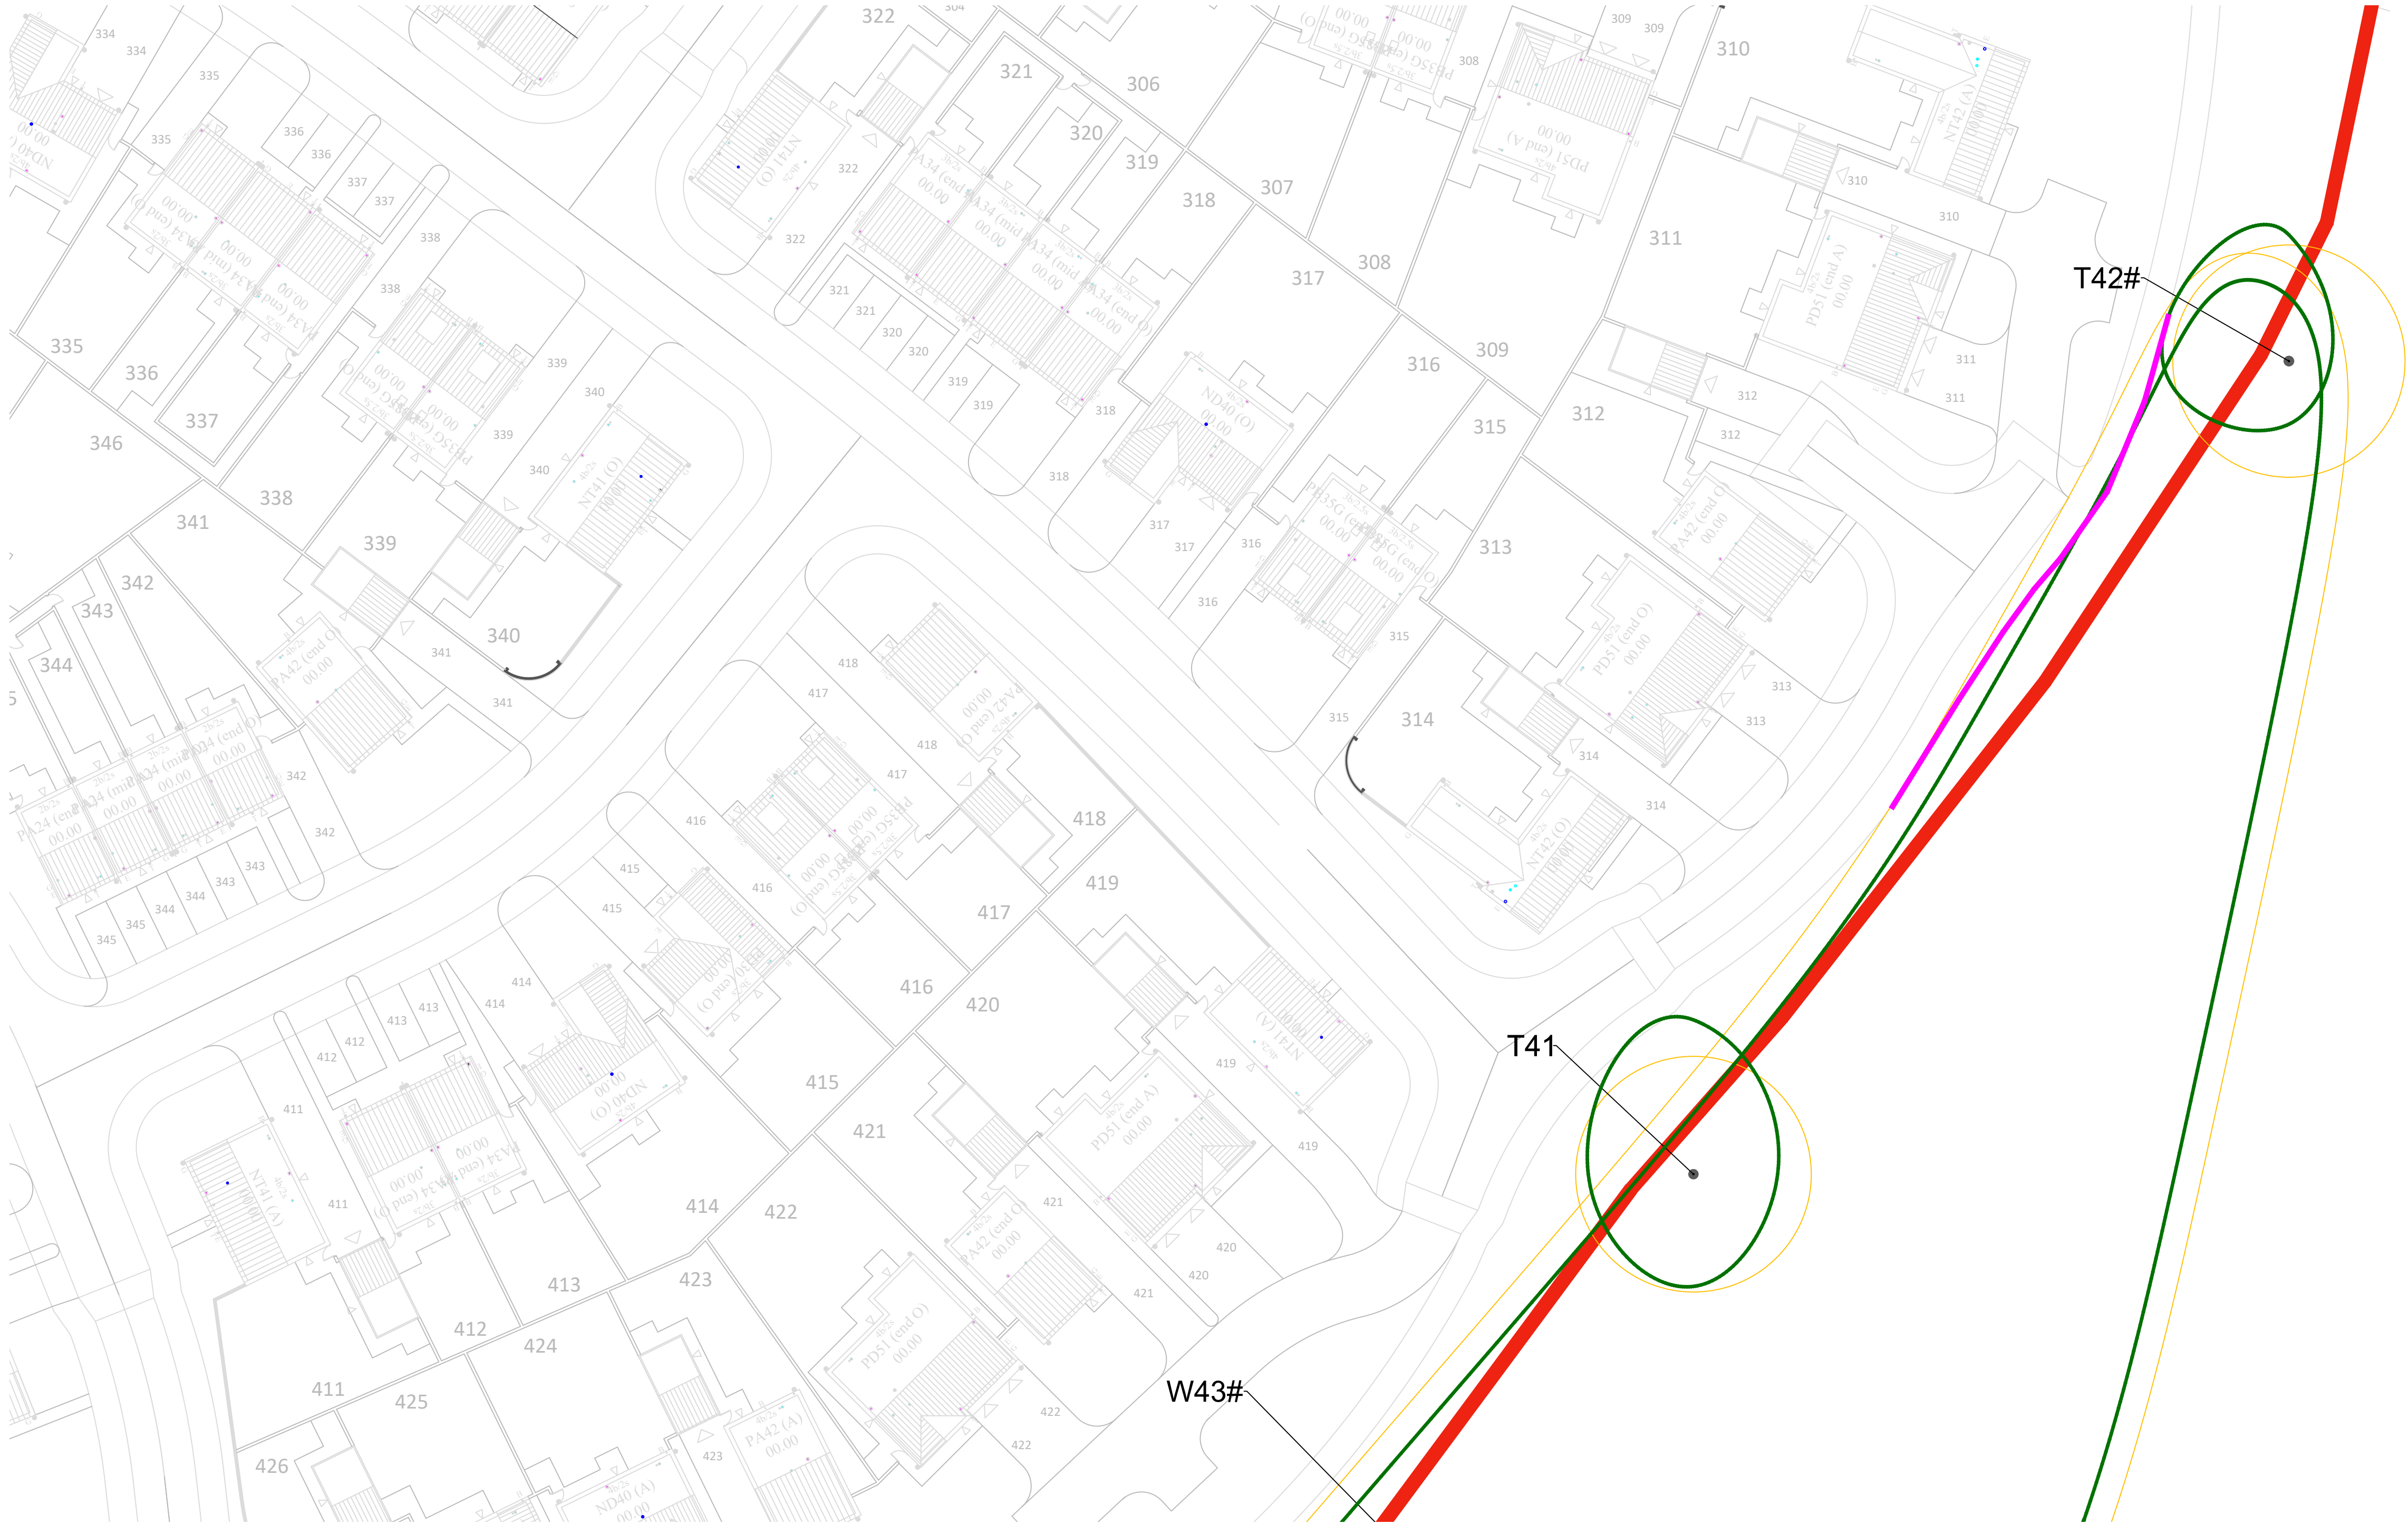

Do not scale this drawing (printed or electronic version).

Contractors must check all dimensions from site.

This drawing is copyright and is for use on this site only. This drawing should be read in conjunction with all relevant consultants drawings and specialist subcontractors / supply chain drawings and specifications.

At works to be carried out in accordance with the latest British Standards / Codes of Practice unless specifically directed otherwise in the specification.

Responsibility for the reproduction of this drawing in paper form, or issued in electronic format, lies with the recipient to check that all information has been replicated in full and is correct when compared to the original paper or electronic image.

Graphical representations of equipment on this drawing have been co-ordinated, but are approximations only. Please refer to the specifications and / or details for actual sizes and / or specific contractor construction information.

Notes:-

Category A tree, group or hedge

Category B tree, group or hedge

Category C tree, group or hedge

Category U tree, group or hedge

Retained tree

Root Protection Area (RPA)

Position estimated on site

Supervised Root Pruning

REV.

DATE

DESCRIPTION

DRAWN

CHK'D

U R B A N
G R E E N

A:

Ground Floor, The Tower,
Deva City Office Park, Trinity Way,
Manchester M3 7BF

T:

+44 (0) 161 312 3131

weareurbangreen.co.uk

Client:

TAYLOR WIMPEY

Project:

STANDEN FARM, PENDLE ROAD,
CLITHEROE PHASE 2, 3 & 4

Title:

ARBORICULTURAL
METHOD STATEMENT

Issue:

PLANNING

Drawn:

KO

Checked:

AB

Approved:

KO

Project:

UG132

Scale @ A0:

1:500

Date:

16/03/21

Dwg No:

UG_132_ARB_AMS_02

Revision:

00

Arboricultural Method Statement (AMS)
Standen Farm, Pendle Road, Clitheroe,
Phase 2,3,and 4
Cellular Confinement System

The new surface must utilise a cellular confinement to avoid compaction and undue damage to the rooting environment.

The four general principles that will require strictly upholding when designing a no dig solution within the RPA are:

- Roots must not be severed.
- Ground Levels must not be changed.
- Soil structure must not be damaged by compaction.
- Oxygen and water must be able to diffuse into the soil below.

A cellular confinement system will ensure that no excavation is required. This will therefore lead to an increase in ground levels.

The sequence of events for the installation of the cellular confinement system will be as follows:

1.Remove the surface vegetation within the footprint of the roadway up to 50mm.

2.A 40mm layer of washed sharp sand containing no fines or salt will be spread across the footprint of the roadway filling any hollows. High points must not be compacted though rolling.

3. Appropriate kerbing/edging will be set above ground level. The cellular confinement system may be retained using pins that are driven into the ground and supported by treated timber edging.

4.A geotextile membrane will be laid over the footprint of the roadway with each section overlapping by a minimum of 300mm.



5. Open out and lay the specified layer thickness of cellular (to be confirmed by product manufacturer and engineer) and pin in place between the edging boards. It may be necessary to cut the cellular confinement system to size using a sharp knife or it can be left uncut and folded up against the edgings if preferred.

6.Ensure that the cells are fully expanded by inserting steel fixing pins at approximately 1-2m spacings (depending on specific engineering requirements). Avoid tree root damage during the pinning process.


7. The cells must be filled with clean, open graded angular aggregate, normally in the particle size range of 5mm - 45mm, not single sized or rounded aggregate. The project engineer may determine alternative fill materials.

8. Do not roll the surface, a light vibratory compaction plate (whacker) may be permitted to settle the stone into the cells. Do not contaminate the filled cells with site debris, soil or mud.

9. Install the permeable pavement layer/wearing course

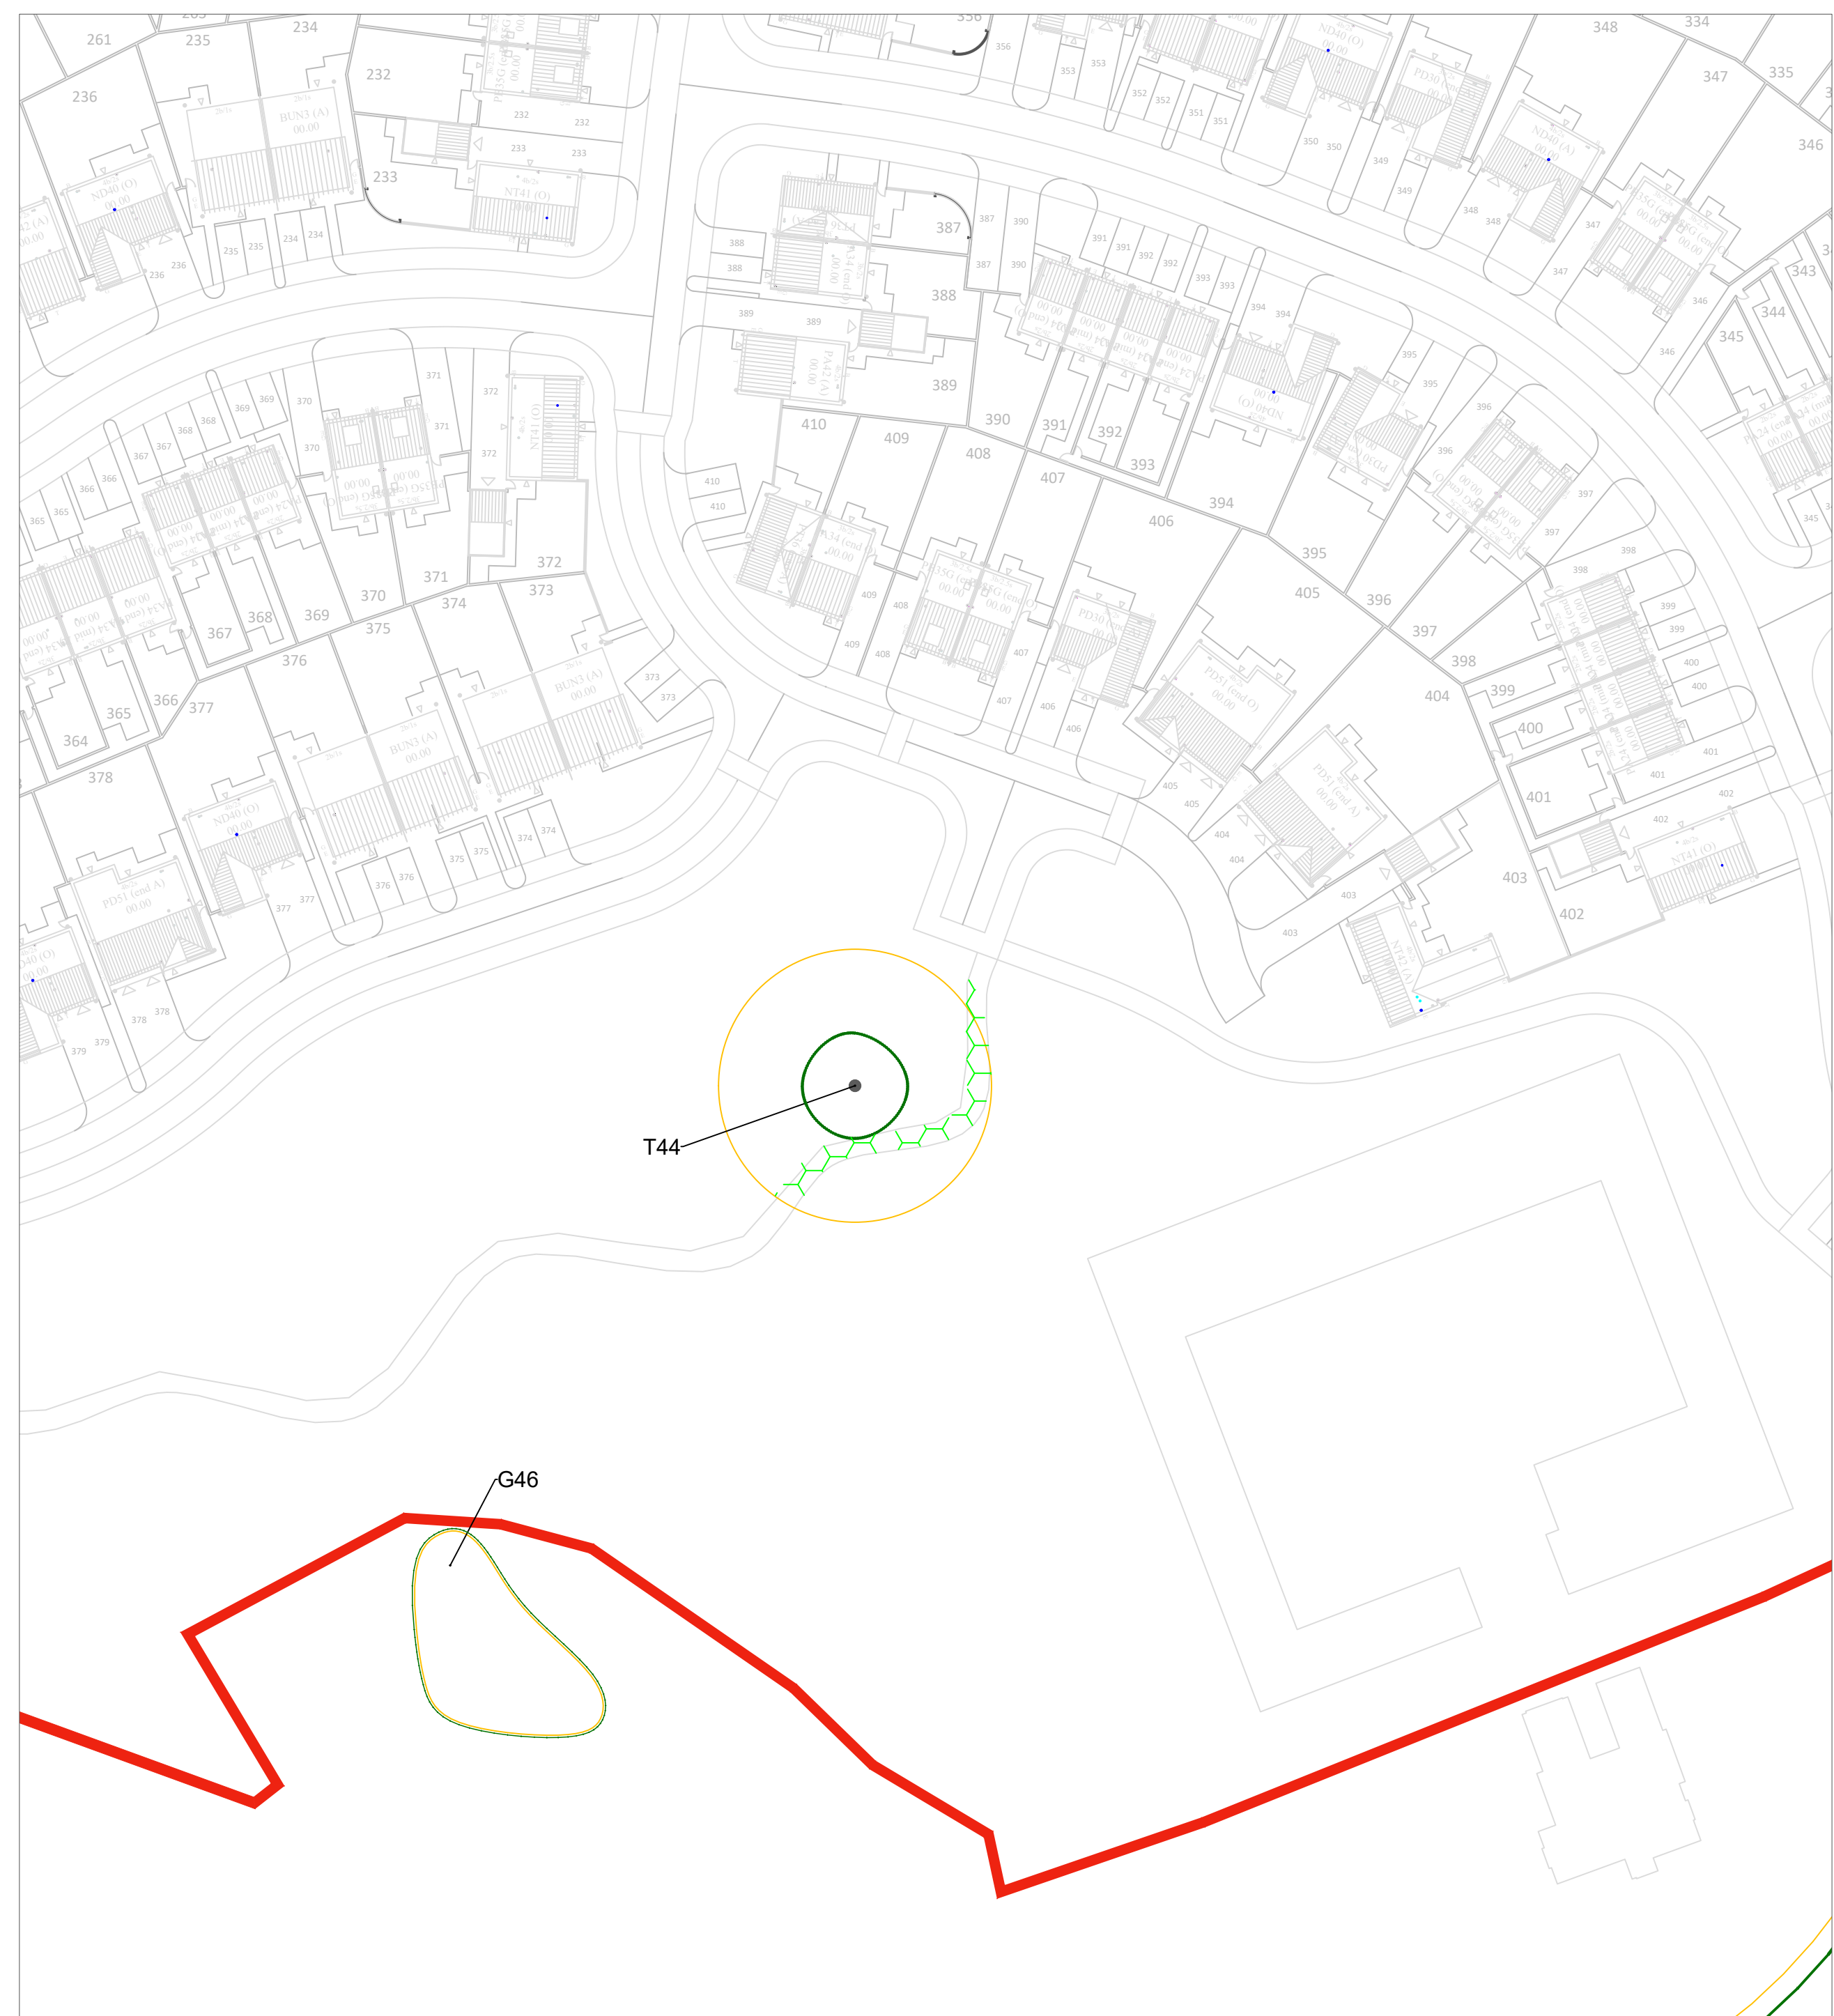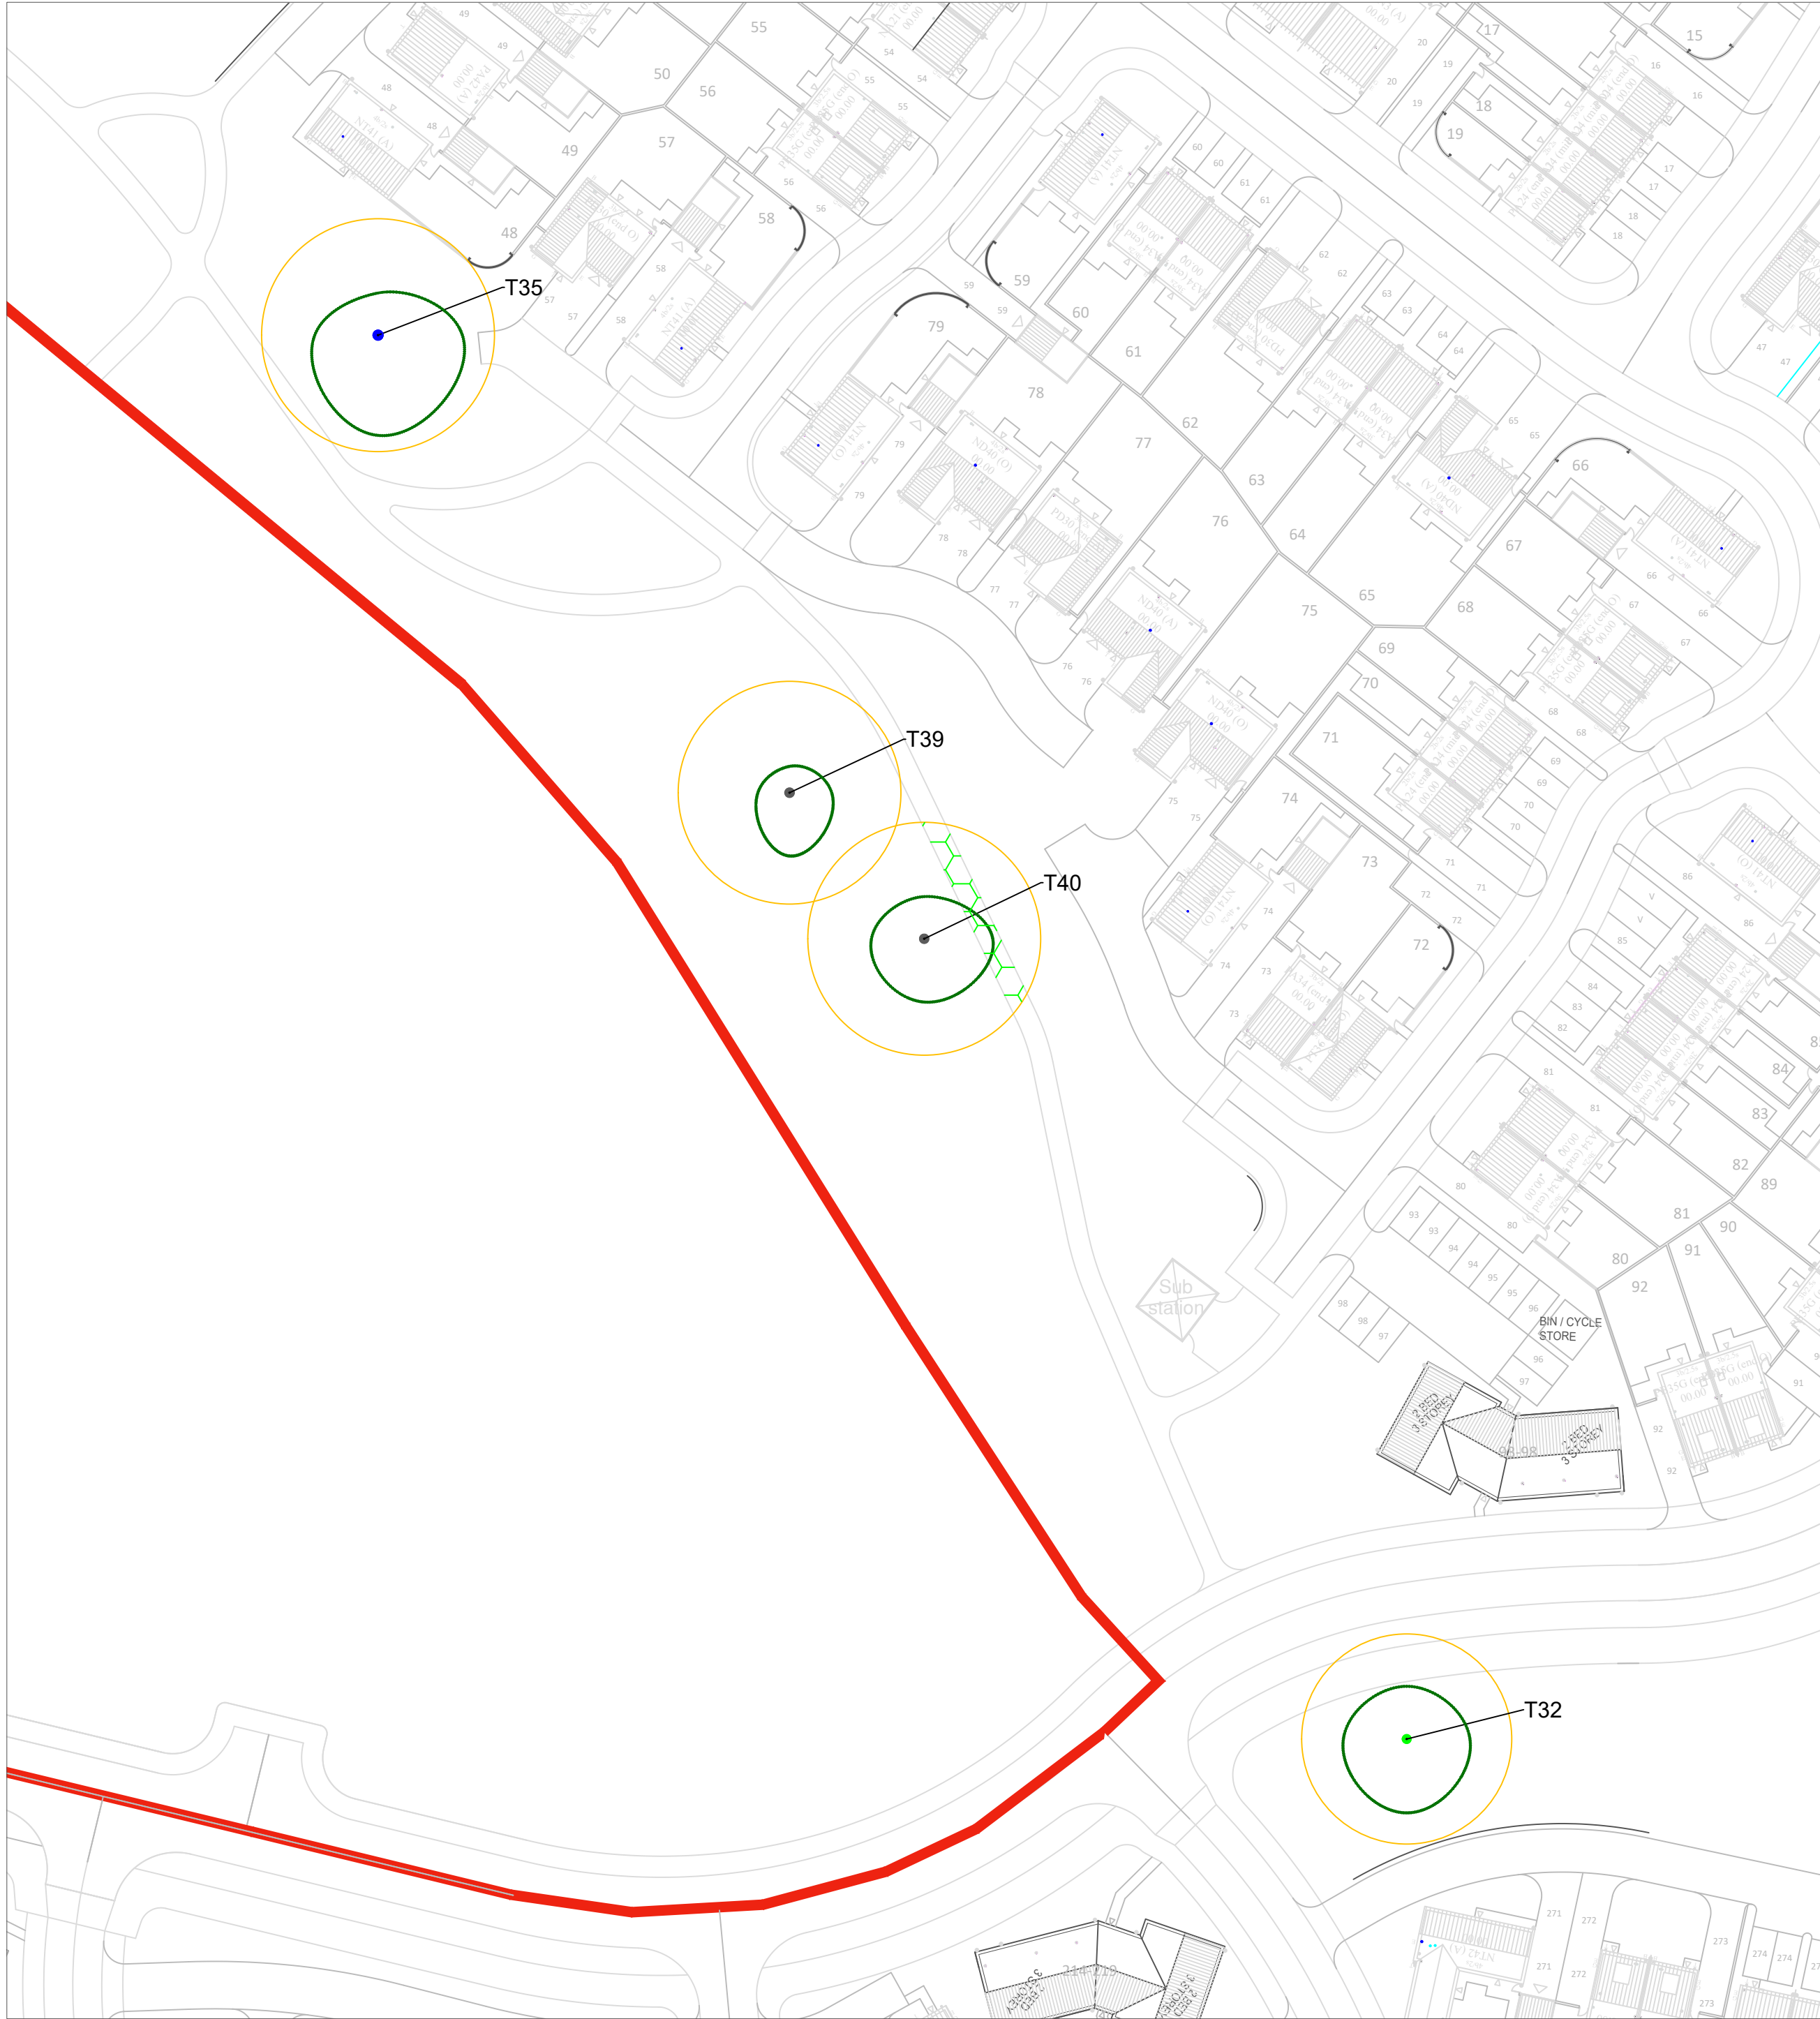

Cellweb 75~200mm Porus Paving Standard Detail

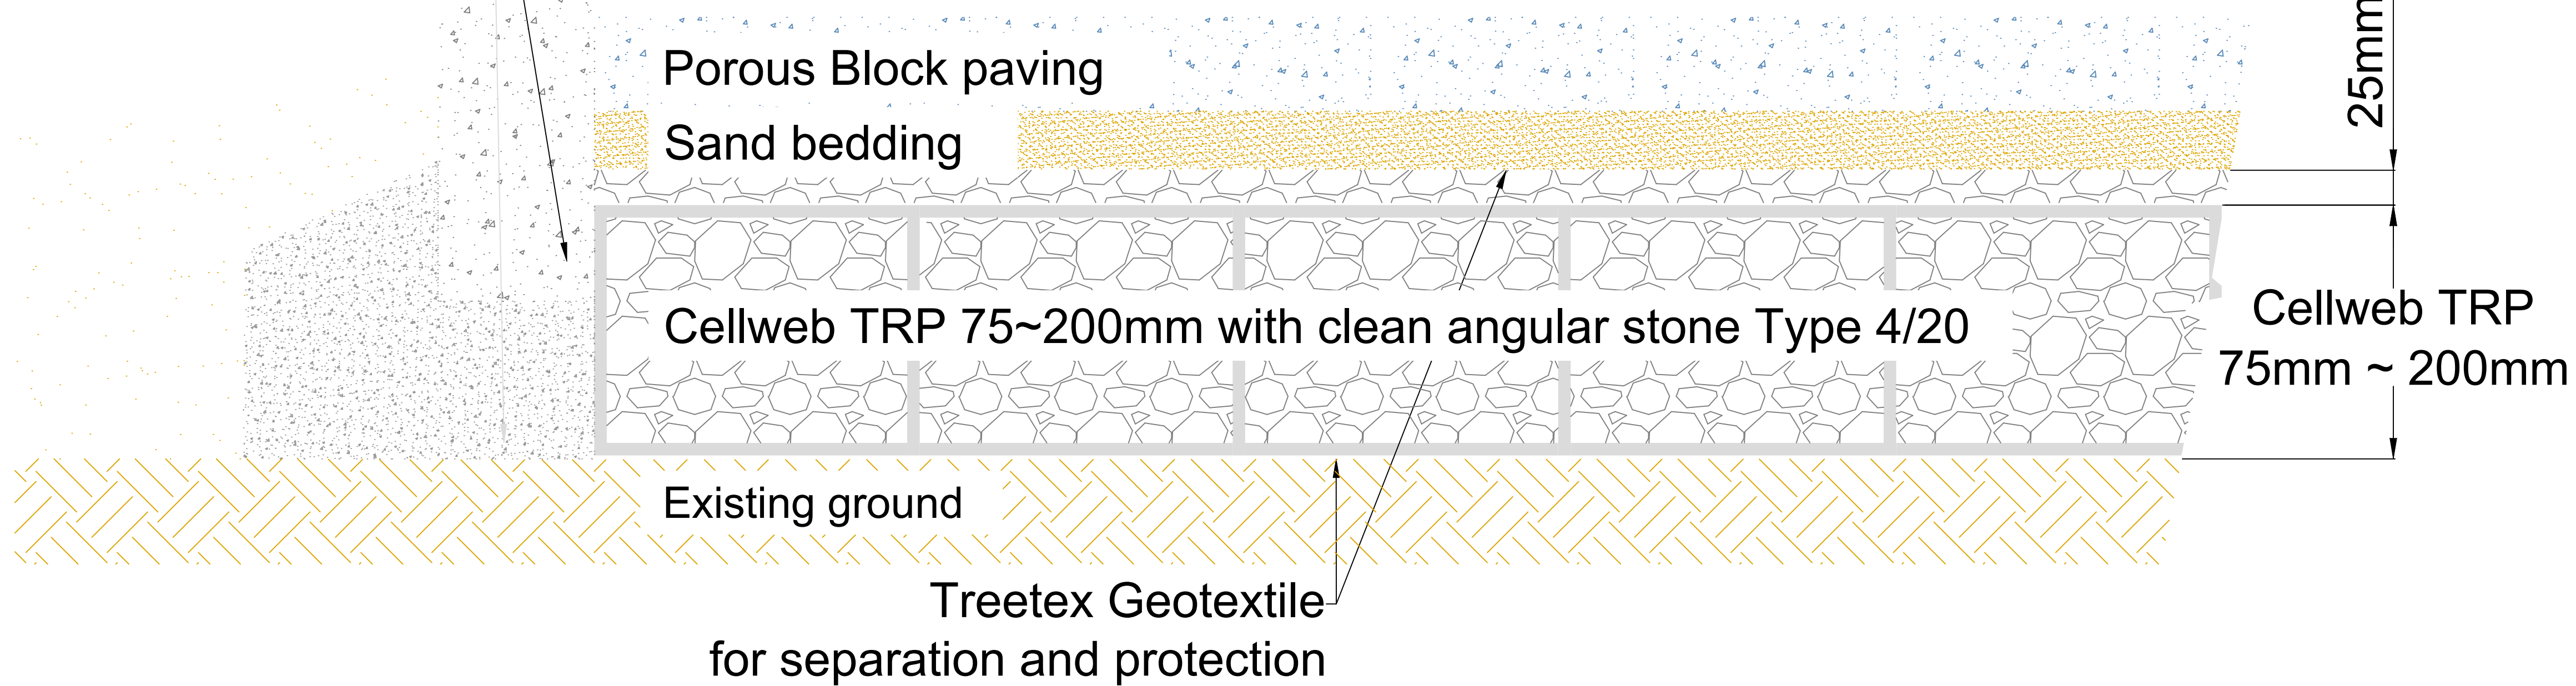

Note: Subbase could be required depending on the existing ground CBR % and the type of traffic on the surface.

Do not scale this drawing (printed or electronic version).

Contractors must check all dimensions from site.


This drawing is copyright and is for use on this site only. This drawing should be read in conjunction with all relevant consultants drawings and specialist subcontractors / supply chain drawings and specifications.

All works to be carried out in accordance with the latest British Standards / Codes of Practice unless specifically directed otherwise in the specification.

Responsibility for the reproduction of this drawing in paper form, or issued in electronic format, lies with the recipient to check that all information has been replicated in full and is correct when compared to the original paper or electronic image.

Graphical representations of equipment on this drawing have been co-ordinated, but are approximations only. Please refer to the specifications and / or details for actual sizes and / or specific contractor construction information.

Notes:-



- | | |
|---|---------------------------------|
|  | Category A tree, group or hedge |
|  | Category B tree, group or hedge |
|  | Category C tree, group or hedge |
|  | Category U tree, group or hedge |
|  | Retained tree |
|  | Root Protection Area (RPA) |
|  | Position estimated on site |
|  | Cultural confinement system |

REV.	DATE	DESCRIPTION	DRAWN	CHK'D					
U R B A N G R E E N A: Ground Floor, The Tower, Deva City Office Park, Trinity Way, Manchester M3 7BF T: +44 (0) 161 312 3131 weareurbangreen.co.uk									
Client:									
TAYLOR WIMPEY									
Project:									
STANDEN FARM, PENDLE ROAD CLITHEROE PHASE 2, 3 & 4									
Title:									
ARBORICULTURAL METHOD STATEMENT									
Issue:									
PLANNING									
Drawn:	KO	Checked:	AB	Approved:	KO				
Project:	UG132	Scale @ AD:	1:500	Date:	16/03/21				
Dwg No:	UG_132_ARB_AMS_03			Revision:	00				

Arboricultural Monitoring Schedule				
Task	Description	Person Responsible	Date	Signed
Work Schedule	Agree timeline of construction works, including key arboricultural works.	Site manager / Arboricultural Consultant		
Inspection of tree works	Ensure that all tree works have been completed in accordance with the schedule and in accordance with BS3998.	Local Authority Tree Officer / Arboricultural Consultant		
Inspection of protective fencing	Inspection of protective fencing prior to any construction works beginning on site to ensure that it is installed in accordance with the Tree Protection Plan.	Arboricultural consultant		
Root pruning	Supervision of hand dig / air spade excavation in accordance with the Tree Protection Plan and root pruning as required by consultant.	Arboricultural consultant		
Hand dig	Excavation by hand of areas shown on the Tree Protection Plan.	Arboricultural consultant		
Installation of cellular confinement system	Cellular confinement system to be installed in accordance with the suppliers specification.	Supplier / Arboricultural consultant		
Inspection of protective fencing	Ad hoc inspection of protective fencing to ensure continued tree protection during construction.	Arboricultural consultant		
Inspection of protective fencing.	Inspection and sign off of protective fencing upon completion of construction prior to its removal.	Arboricultural consultant		

Do not scale this drawing (printed or electronic version).

Contractors must check all dimensions from site


This drawing is copyright and is for use on this site only. This drawing should be read in conjunction with all relevant consultants drawings and specialist subcontractors / supply chain drawings and specifications.

At works to be carried out in accordance with the latest British Standards / Codes of Practice unless specifically directed otherwise in the specification.

Responsibility for the reproduction of this drawing in paper form, or issued in electronic format, lies with the recipient to check that all information has been replicated in full and is correct when compared to the original paper or electronic image.

Graphical representations of equipment on this drawing have been co-ordinated, but are approximations only. Please refer to the specifications and / or details for actual sizes and / or specific contractor construction information.

Notes:-



REV.	DATE	DESCRIPTION	DRAWN	CHK'D

U R B A N
G R E E N

A: Ground Floor, The Tower,
Deva City Office Park, Trinity Way,
Manchester M3 7BF

T: +44 (0) 161 312 3131

weareurbangreen.co.uk

Client:

TAYLOR WIMPEY

Project:

STANDEN FARM, PENDLE ROAD,
CLITHEROE PHASE 2, 3 & 4

Title:

ARBORICULTURAL METHOD
STATEMENT - SIGN OFF

Issue:

PLANNING

Drawn:	Checked:	Approved:
KO	AB	KO
Project:	Scale @ A0:	Date:
UG132	NTS	16/03/21
Dwg No:	Revision:	
UG_132_ARB_AMS_04	00	
