


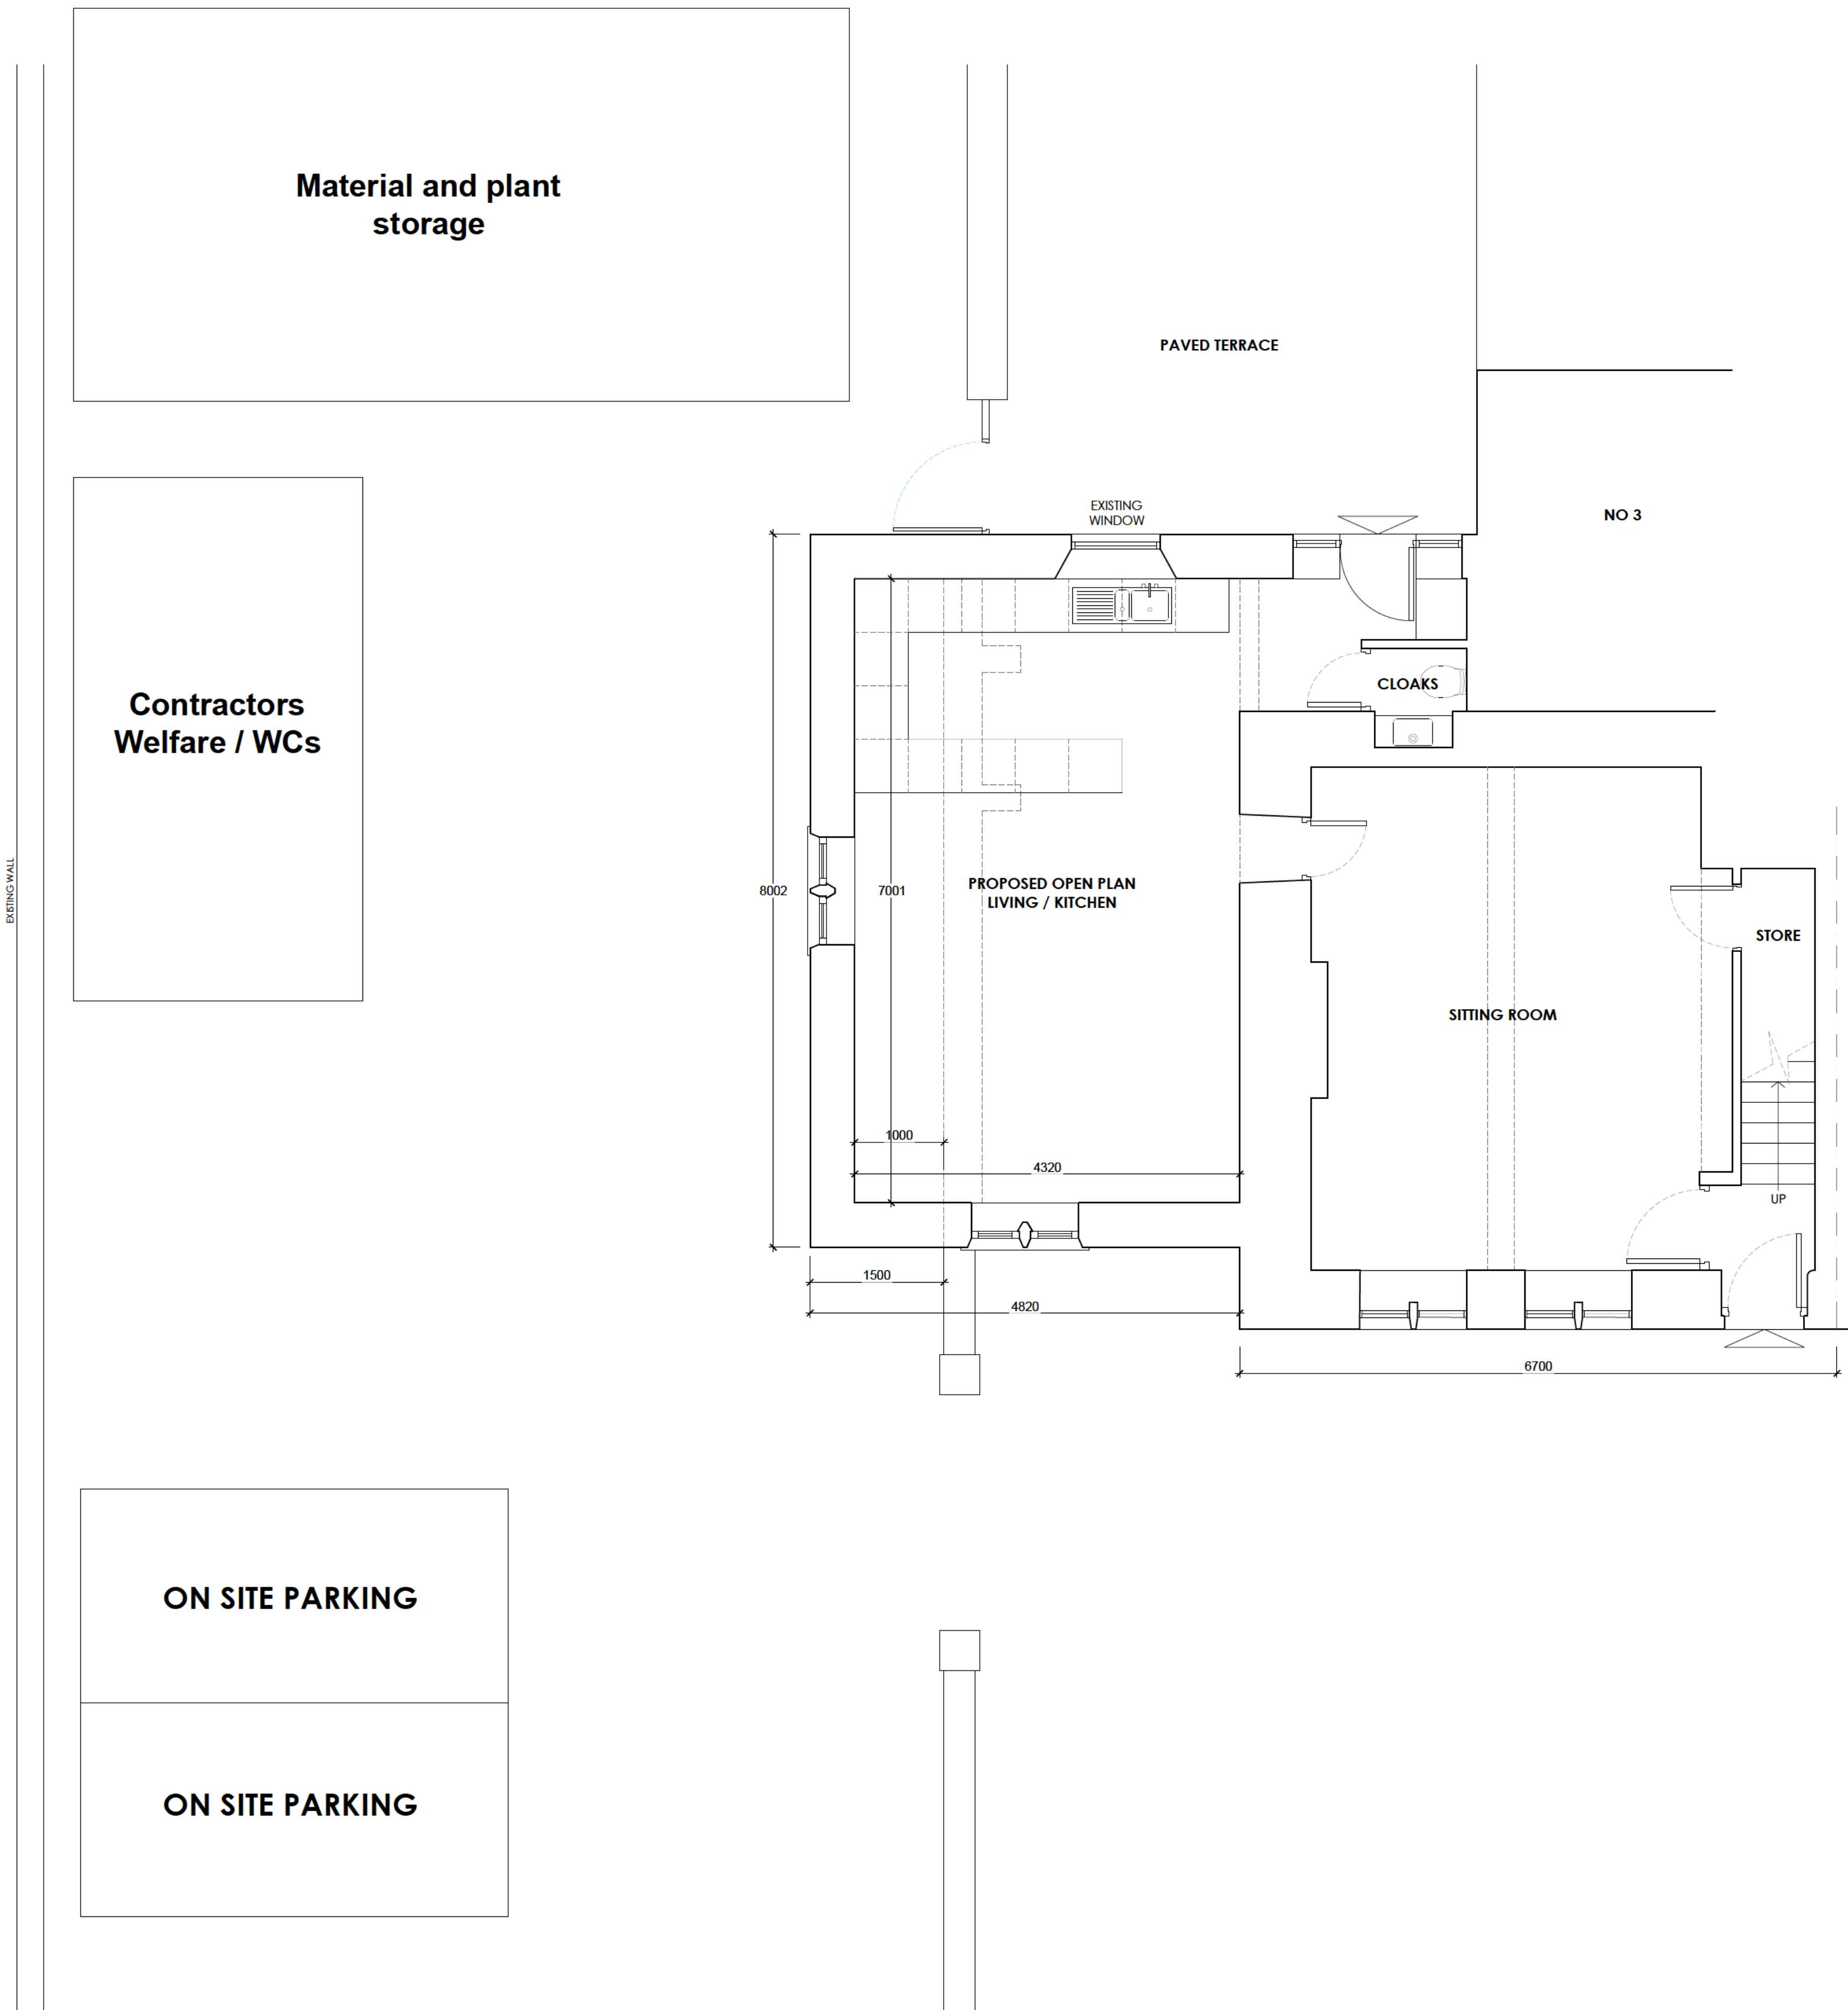

Construction Method Statement

Emergency Contact Number:
Aisling Carruthers [REDACTED]

Unless otherwise approved in writing by the Local Planning Authority, all works and ancillary works, including the use of equipment or deliveries to the site, shall be carried out only between 0800 hours and 1700 hours on Mondays to Fridays between 0900 hours and 1300 hours on Saturdays and at no time on Sundays, Bank Holidays or Public Holidays. A permission is sought for works to be carried out outside the hours stated, applications in writing must be made with seven days' notice to Ribbles Valley Borough Council. HGV deliveries to the approved development shall only be accepted between the hours of 9:00am and 14:30pm Monday to Friday, to avoid peak traffic on the surrounding highway network. Site operatives and visitors vehicles to be parked on site where possible. Signage to be provided to clearly indicate parking area near to secure entrance of contractors compound.

Hera security fence to be provided around the perimeter of the extension works site with lockable access gate to the site. Warning signs "NOT TO ENTER" to be fixed to security fence. The full perimeter security fence to remain the responsibility of the Principal Contractor throughout the construction phase.

Loading and unloading of plant and materials to be carried out on / adjacent to site. All plant and materials to be unloaded and stored within the designated fenced site area.

The Principal Contractor shall: Arrange for the induction of all personnel coming on to the site; ensure that all those engaged on the works wear suitable identity badges which shall be visible at all times; keep dangerous tools securely stored where possible; keep all of those engaged on the works to the site of the works and keep unauthorised persons off the site; ensure proper supervision of the works at all times.

Arrangements for Welfare Provision: The Principal Contractor will arrange for on site welfare facilities to comply with Regulations 2015 Schedule 2.

Storage of plant and materials to be stored within site compound. All plant to be stored on site in an orderly manner. Fuel to be removed and isolators if fitted to be activated. No fuel to be stored on site. Generally required materials to be stored to their place of work where possible in an orderly fashion. Contractor to program the delivery of materials to ensure they are delivered to site when required only.

Hand operated wheel and plant washing facilities to be provided adjacent to works site entrance to allow for hosing and washing of vehicles. To reduce the pollution risk Contractor to ensure:

- plant and wheel washing is carried out in a designated area of hard standing at least 10 metres from any watercourse or surface water drain.
- run-off is collected in a sump - (recycle and re-use water where possible).
- settled solids are removed regularly and into a skip and to licensed recycling centre.
- discharge of contained water to go into foul sewer with prior permission from United Utilities - or if permission is not granted Contractor to make arrangements for water to be tankered off site for authorized disposal.

Control of dust and dirt. During extreme weather conditions such as high winds, dust generating site operations shall be suspended and all exposed areas covered or treated with water spray to ensure dust does not become airborne and affect adjacent dwellings. Any potential dusty materials to be covered and securely stored on site where applicable. The most appropriate method of controlling dust from site tools is water suppression - to be implemented on site by Contractor. No burning of materials or waste on site.

Contractor to arrange for waste to be removed from site and taken to a licensed recycling centre.

Contractor to ensure vehicles do not impede roads or neighbouring properties. Contractor to organize all deliveries to arrive at peak times and also when sufficient labour is on site to efficiently off load materials.

Contractor to provide risk assessments for all construction work and be responsible for all on site health and safety. The site manager shall ensure that the site is kept clean and tidy at all times. Cleanliness of site and access road to be continually reviewed by site manager and mechanical sweeping to be carried out when necessary.
