



LAKELAND
TREE CONSULTANCY
ARBORICULTURAL PLANNING SPECIALIST

Arboricultural Impact Assessment

Rose Hill Farm
Whalley Old Road
Billington
BB7 9JF

June 2026

Project details

Job no.	LTC336
Site	Rose Hill Farm, Whalley Old Road, Billington, BB7 9JF
Client	Damian Hanson
Agent	Zara Moon Architects
Arboriculturist	Jennie Keighley PhD MSc MArborA
Local authority	Ribble Valley Borough Council
Date	22 June 2026
Issue	Final issue for planning

Lakeland Tree Consultancy

Halton Mill, Mill Lane

Halton, Lancashire

LA2 6ND

01524 874124

info@lakelandtreeconsultancy.co.uk



Contents

	Page no.
1. Executive Summary	1
2. Introduction	2
3. The Site and Tree Population.....	3
4. The Development Proposal and Arboricultural Impact Assessment	6
5. Protection of Retained Trees.....	9
6. Tree Preservation Orders, Conservation Areas and Other Legal Constraints.....	12
References	14

Appendices

Tree Survey Plan
Tree Protection Plan
BS5837 Tree Protection Fencing
BS5837 Tree Survey Schedule

1. Executive Summary

- 1.1 This arboricultural impact assessment (AIA) relates to a planning application at Rose Hill Farm, Billington for the proposed construction of a new access lane.
- 1.2 A tree survey carried out in accordance with BS5837 identified four individual trees, six groups of trees, and a hedge across the wider site. One of the individual trees was identified as being a high-quality veteran tree.
- 1.3 Assessment of the proposal indicates that construction of the development will not require the removal of any of the existing trees or hedging and there is not projected to be any requirement for facilitation pruning works.
- 1.4 The existing trees and hedging can be adequately protected by means of temporary tree protection fencing, which is to be laid-out as shown on the appended Tree Protection Plan, and by following both the site-specific and general tree protection recommendations provided herein.

2. Introduction

- 2.1 The client's agent instructed Lakeland Tree Consultancy to survey the trees at Rose Hill Farm (formerly Smalleys Farm House), Whalley Old Road, Billington and undertake an AIA in relation to a planning application for the proposed construction of a new access lane.
- 2.2 Arboriculturist Jennie Keighley PhD MSc MArborA visited the site on 8th May 2025 and surveyed all trees with reasonable potential to be impacted by the proposed works in accordance with the British Standard guidance, BS5837 (2012) *Trees in relation to design, demolition and construction - Recommendations*. The site was subsequently resurveyed on 10th February 2026.
- 2.3 This report will assess the potential impacts of the proposed development upon the existing tree population and outline the tree protection measures needed to prevent retained trees from being damaged during the construction works. It should be supplied to the Local Planning Authority (LPA) to allow them to determine the planning application and its contents should be adhered to by the appointed contractor, should the development be approved.

3. The Site and Tree Population

The site

3.1 The site is in a rural location between the villages of Langho and Billington, Lancashire, and is currently part of a steep, north-west-facing field of agricultural pasture (see Figure 1). The site is bounded to the north by Rose Hill Farm, to the east and west by further extents of the field, and to the south by Whalley Old Road. There is an existing, unmade agricultural access into the field from Whalley Old Road via a metal field gate, and an independent timber pedestrian gate leading onto the public right of way that runs adjacent to the western field boundary.



Figure 1: Google Earth image of application site
(dated 1 May 2025)

The tree population

3.2 There are established belts of native deciduous trees running along the east and west field boundaries, most of which are growing beyond the fence lines. Clusters of smaller trees and shrubs, predominantly holly, gorse and hawthorn, can be found around the field edges. There is a native mix group growing along the Whalley Old Road frontage comprising a grown-out hedge and young self-set trees. A large beech tree sits near the northern field boundary.

3.3 A BS5837 tree survey identified four individual trees, six groups of trees and a hedge across the wider site. These were located both within the client's ownership and on areas of immediately adjacent land. The positions of the surveyed trees in relation to the existing site are shown on the appended Tree Survey Plan.

3.4 The retention value of the surveyed trees was categorised using the guidance given in Table 1 of BS5837 (2012), which is explained in the appended Tree Survey Schedule. One individual tree was categorised as high quality (A-category), two trees and two groups were categorised as moderate quality (B-category) and one tree, four groups and the hedge were categorised as low quality (C-category).

Veteran trees

3.5 Trees classified as veteran or ancient are of exceptionally high value and are afforded special consideration as "irreplaceable habitats" within the National Planning Policy Framework (NPPF). The tree survey identified one veteran tree at this site, as defined by Lonsdale (2013). Beech T3 (Photographs 1 and 2) was found to be exhibiting signs of advanced age, including a very large stem diameter, with a second large codominant stem previously removed near ground level. Significant stem decay is evidenced by numerous fungus brackets of white rot decay species *Ganoderma australe* growing around the full circumference of the base. Further veteran characteristics include flaking bark, knotholes and deadwood.



Photograph 1: Veteran beech T3,
showing codominant stem previously removed



Photograph 2: Veteran beech T3,
showing general form and evident failure at apex

3.6 Veteran and ancient trees are invaluable reservoirs for biodiversity and may also be of cultural or heritage significance. It is imperative that they are retained and protected from development works by following the guidance outlined in Section 5.

4. The Development Proposal and Arboricultural Impact Assessment

The development proposal

- 4.1 The Proposed Site Plan (drawing number 219.25 03 by Zara Moon Architects) indicates that the planning application is for the proposed construction of a new access lane linking Rose Hill Farm with Whalley Old Road. The new lane will follow an existing natural line that currently snakes up the field. A five-bar timber field gate will be sited at the new Whalley Old Road entrance, with lengths of three-bar post and rail fence to either side.

Services and drainage

- 4.2 There is not anticipated to be any requirement for new services or drainage as part of this development. If new provisions, such as service trenches or drainage features *are* required, they should be sited so as to avoid the root protection areas (RPAs) of retained trees and hedges wherever possible. Where the installation of services or drainage within RPAs cannot be avoided, excavation must be carried out using hand-held tools only and in accordance with the NJUG Volume 4 guidance, taking care to minimise any root damage.

Tree/hedge removals

- 4.3 Assessment of the proposal indicates that construction of the development will not require the removal of any of the existing trees or hedging.

Tree works

- 4.4 There is not projected to be any requirement for facilitation pruning works at this site. If tree works *are* found to be required, they should be carried out by a suitably qualified, experienced and insured arborist, taking account of nesting bird season (from March to August inclusive), and must be in accordance with the British Standard guidance BS3998 (2010) *Tree work - Recommendations*.

RPA encroachments

- 4.5 As shown on the appended Tree Protection Plan, proposed works within or close to the RPAs of retained trees include: -
- Cut and fill operations likely to encroach close to RPAs of tree T3 and groups G1 and G5

The above operations have potential to impact tree RPAs and must be carried out in accordance with the preliminary arboricultural method statement and general tree protection requirements provided later in Section 5.

Future tree pressures

4.6 The AIA seeks to identify any reasonably foreseeable sources of conflict between the existing trees and the proposed development that would lead to future pressure to remove or significantly prune the trees. This can include shading issues and nuisance issues, such as the dropping of fruit or leaf litter. The assessment does not include proposed new trees, the details of which may not have been available at the time this report was prepared.

4.7 No specific future tree pressures have been identified in relation to the proposed development at this site.

5. Protection of Retained Trees

Tree protection fencing

- 5.1 Adequate protection of the retained trees during the development is paramount in ensuring their future health and survival. Creating a construction exclusion zone by erecting temporary fencing around the perimeter of the trees' RPAs is the most effective way of protecting them during the works. It is important that tree protection fencing is secured into the ground, so that it cannot be easily moved or shunted out of place whilst the construction works are underway.
- 5.2 For the development in question, the default BS5837 tree protection fencing specification, as shown on the appended illustration, is expected to be suitable. It may be possible to agree an alternative fencing specification with the LPA Tree Officer prior to commencement, if required. The fencing is to be laid-out as indicated on the appended Tree Protection Plan prior to any works on site, including site preparation, demolition and deliveries, and shall remain in place until construction is complete and all associated materials have been removed from site.
- 5.3 Once erected, the tree protection fencing shall be labelled at regular intervals with all-weather notices stating 'TREE PROTECTION AREA - KEEP OUT!'. The construction exclusion zone shall be considered sacrosanct and the tree protection fencing must be kept well-maintained and functional for the duration of the construction works. Any form of construction access, including storage of materials, equipment, stone or earth and tracking of vehicles or plant, is prohibited within the construction exclusion zone.

Preliminary arboricultural method statement

5.4 An arboricultural method statement intends to identify site operations with reasonably foreseeable potential to adversely impact the health of trees within or close to the development site and outlines the necessary actions and precautions required during the development process to minimise the risk of causing damage to trees (see Table 3, below).

5.5 As this arboricultural method statement is provided pre-determination, it should be considered preliminary, pending the confirmation of all design details, such as services, drainage, boundary treatments and detailed construction specifications. A detailed arboricultural method statement, including a sequence of works and programme of site monitoring and arboricultural supervision, can be conditioned to a planning approval, where necessary.

Table 3: Site-specific guidance for operations within tree RPAs

Operation	BS5837 Guidance
Cut and fill operations	• The cut and fill operations to form required ground levels for the new access lane have potential to encroach towards the RPAs of veteran tree T3 and groups G1 and G5 • To prevent construction operations from encroaching within the RPAs, temporary BS5837-specification tree protection fencing shall be erected at the three pinch points indicated on the appended Tree Protection Plan, where the lane is closest to the trees, prior to the commencement of any works on site • The fencing shall be secured into the ground, so that it cannot be moved or shunted out of place • The fencing shall be kept well-maintained and functional for the full duration of the works • The construction exclusion zones indicated on the appended Tree Protection Plan shall be considered sacrosanct and there shall be strictly no tracking of vehicles or plant, or storage, deposition or redistribution of stone, earth, materials, or equipment within these areas

5.6 General tree protection requirements

- The tree protection fencing shall be installed prior to any works on site, including site preparation, demolition and deliveries
- The tree protection fencing shall be kept well-maintained and functional for the duration of the works and shall not be moved until construction is complete and all associated materials have been removed from site
- Vehicles and plant shall not operate within RPAs, unless there is an existing hard surface in place or load-appropriate ground protection has been installed
- Soil levels within RPAs shall not be raised or lowered, unless authorised in advance by the LPA
- Soil within RPAs shall not be scraped, skimmed or mechanically compacted. The majority of tree roots are found in the top 600mm of soil, so even a shallow scrape can cause detrimental root damage
- Materials, equipment, vehicles, skips, demolition arisings, stone or earth shall not be stored within soft-surfaced RPAs
- Oil, fuel, chemicals, cement or any other material with potential to cause damage to trees shall not be poured, stored, mixed, washed or discharged within tree RPAs. Consideration shall also be given to the topography of the site to prevent materials running towards trees
- Services and drainage shall not be installed below ground level within RPAs, unless authorised in advance by the LPA
- Surface water run-off shall not be re-diverted into or out of tree RPAs
- Fires shall not be lit within 10m of any tree crown or RPA
- Temporary buildings, including welfare units and portable toilets, shall not be sited within soft-surfaced RPAs
- Notice boards, telephone cables, anchorage for equipment or any other services shall not be attached to trees
- Deliveries by crane or tipper truck shall be supervised by the site manager, ensuring the vehicle operates in a manner in which trees are not put at risk of damage
- Incidents of damage to a tree or with potential to damage a tree, such as an incursion, accident, impact or spillage, shall be logged and reported to the Project Arboriculturist forthwith, who will advise on the nature and timescale of any remedial action required

6. Tree Preservation Orders, Conservation Areas and Other Legal Constraints

- 6.1 Trees may be subject to legal protection, by means of being covered by a Tree Preservation Order (TPO) or by being located within a Conservation Area. It is an offence to cut down, uproot, top, lop, cause wilful damage or destruction of protected trees without the appropriate consent from the Local Authority. Fines for carrying out unauthorised works to protected trees can be considerable. The Local Authority must be given six-weeks' notice prior to the removal of trees within a Conservation Area with a stem diameter greater than 75mm (at a height of 1.5m above ground level). To carry out works on trees covered by a TPO, a formal application must be made to the Local Authority, which should be determined within an eight-week period.
- 6.2 According to Ribble Valley Borough Council's website (www.ribblevalley.gov.uk; searched 17/02/26), the site is not located within a Conservation Area. The website does not include an interactive TPO map or search function, so the presence of any TPOs would need to be checked with the Council directly. It is always advisable to check for any statutory tree protection directly with the Council prior to carrying out any tree works that are not authorised as part of a detailed planning approval.
- 6.3 It should be noted that, subject to certain exemptions, a felling license must be obtained from the Forestry Commission for felling of trees that will equate to more than five cubic metres of timber in a calendar quarter. This does not, however, apply to tree removals that are authorised under a detailed planning approval.

6.4 Hedgerows meeting a particular series of criteria may be classed as 'important' and afforded legal protection under the Hedgerows Regulations 1997. It is an offence to remove an important hedgerow without appropriate consent from the Local Authority.

6.5 Birds, bats and certain other species are protected by the Wildlife and Countryside Act 1981. It is an offence to disturb wild birds within the nesting season (from March to August inclusive) and bats at any time of year, and this must be taken into account whilst carrying out tree works. The advice of a suitably qualified and licensed ecologist must be sought if the presence of birds, bats or other protected species is identified before or during tree works.

References


British Standards Institute (2012) *BS5837 Trees in relation to design, demolition and construction - Recommendations*

British Standards Institute (2010) *BS3998 Tree work - Recommendations*






Lonsdale, D. (ed.) (2013) *Ancient and other veteran trees: further guidance on management*. The Tree Council, London

The National Joint Utilities Group (2007) *Volume 4 - NJUG Guidelines for the planning, installation and maintenance of utility apparatus in proximity to trees*

Tree Survey Plan



BS5837 Tree retention categories:

-  Category A
High quality tree
-  Category B
Moderate quality tree
-  Category C
Low quality tree
-  Category U
Unsuitable for retention
-  Root protection areas (RPAs)

Identification numbers:

T = individual tree
G = group of trees
W = woodland
H = hedge

Site:
Rose Hill Farm
Whalley Old Road
Billington
BB7 9JF

Client:
Damian Hanson

Date: February 2026

Scale: 1:500 at A2

Drawing: LTC336-TSP Rev A

Drawn by: JK







Tree Survey Schedule Summary		
ID	Species	Cat.
T1	Maple	B
T2	Sycamore	B
T3	Beech	A
T4	Birch	C
G1	Native mix	B
G2	5no. hawthorn, holly	C
G3	Gorse	C
G4	Native mix	C
G5	Native mix	B
G6	≈13no. holly, hazel, hawthorn	C
H1	Native mix	C

Site Plan
as Existing



Halton Mill, Mill Lane, Halton, LA2 6ND
info@lakelandtreeconsultancy.co.uk
01524 874124

Tree Protection Plan

-  Category A
High quality tree
-  Category B
Moderate quality tree
-  Category C
Low quality tree
-  Category U
Unsuitable for retention
-  Root protection areas (RPAs)
-  Construction exclusion zone and temporary tree protection fencing

Identification numbers:

T = individual tree
G = group of trees
W = woodland
H = hedge

Site:

Rose Hill Farm
Whalley Old Road
Billington
BB7 9JF

Client:

Damian Hanson

Date: June 2026

Scale: 1:500 at A2


Drawing: LTC336-TPP Rev B

Drawn by: JK



LAKELAND
TREE CONSULTANCY
ARBORICULTURAL PLANNING SPECIALIST

Halton Mill, Mill Lane, Halton, LA2 6ND
info@lakelandtreeconsultancy.co.uk
01524 874124



Site Plan as Proposed

There must be no ground disturbance, levels changes, soil compaction or excavation within any part of the RPA of veteran tree T3

PROW retained as existing

PROW access remains open

BS5837-specification tree protection fence to be erected prior to any works on site, including site preparation and deliveries

Stone or earth from cut and fill operations to form new access lane shall not be stored, redistributed or deposited within construction exclusion zones

No construction access near groups G1 or G3


BS5837-specification tree protection fence to be erected prior to any works on site

No construction access near group G5

No construction access near group G4

BS5837-specification tree protection fence to be erected prior to any works on site

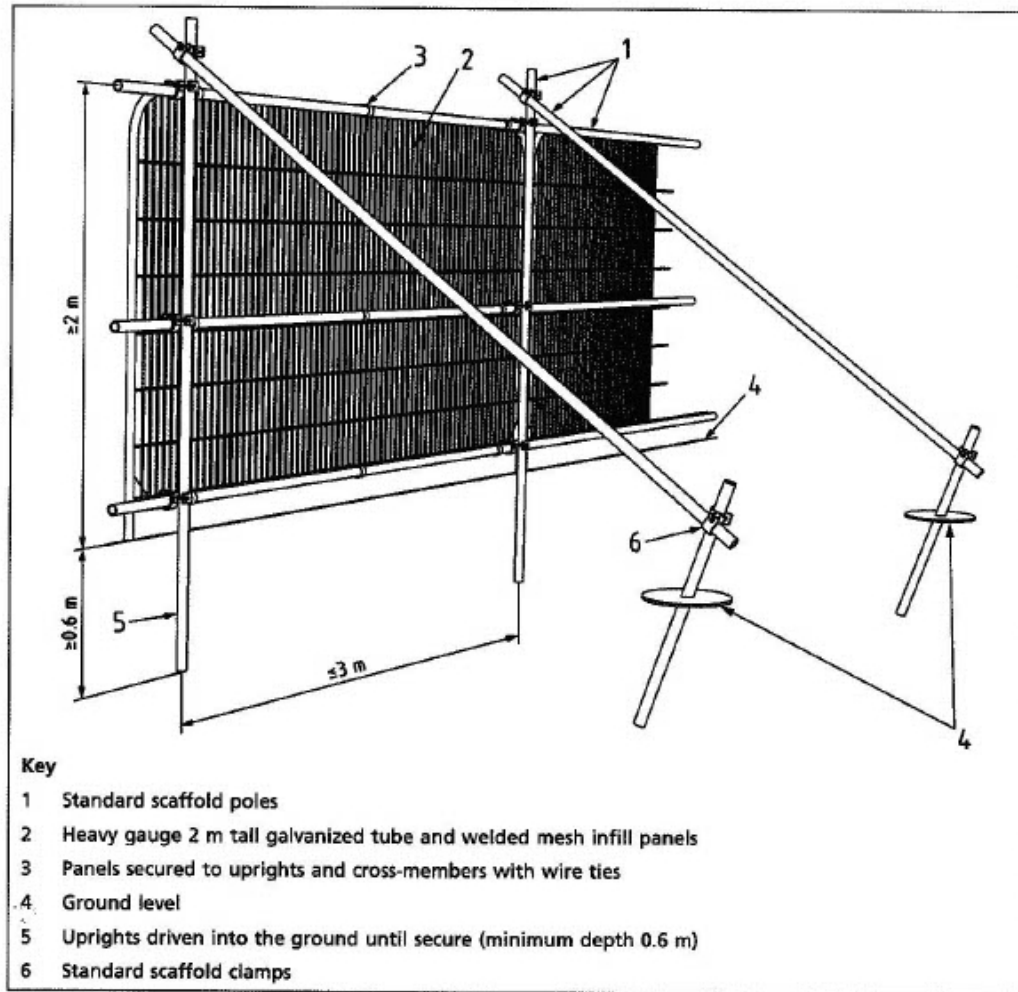BS5837 Tree Protection Fencing



Reproduced from BS 5837:2012 *Trees in relation to design, demolition and construction – Recommendations*, BSI Standards Institution 2012.

TREE PROTECTION AREA KEEP OUT!

TREES ENCLOSED BY THIS FENCE ARE PROTECTED BY PLANNING CONDITIONS AND ARE SUBJECTS OF A
TREE PRESERVATION ORDER
(TOWN & COUNTRY PLANNING ACT 1990)

CONTRAVENTION OF TREE PRESERVATION ORDER MAY LEAD TO CRIMINAL PROSECUTION

THE FOLLOWING **MUST** BE OBSERVED BY ALL PERSONS:-

- THE PROTECTIVE FENCING MUST NOT BE REMOVED
- NO PERSON SHALL ENTER THE PROTECTED AREA
- NO MACHINE OR PLANT SHALL ENTER THE PROTECTED AREA
- NO MATERIALS SHALL BE STORED IN THE PROTECTED AREA
- NO SPOIL SHALL BE DEPOSITED IN THE PROTECTED AREA
- NO EXCAVATION SHALL OCCUR IN THE PROTECTED AREA

ANY INCURSION INTO THE PROTECTED AREA MUST BE
WITH THE WRITTEN PERMISSION OF THE LOCAL PLANNING AUTHORITY

Tree protection fencing shall be installed as shown in the specification on the left and shall be labelled at regular intervals with all-weather notices, such as that shown above, stating "TREE PROTECTION AREA - KEEP OUT!"

BS5837 Tree Survey Schedule

The trees surveyed have been assigned one of the following categories, in line with the guidance outlined in British Standard 5837 (2012)

Trees in relation to design, demolition and construction - Recommendations: -

A

Trees of **high quality** with an estimated remaining life expectancy of at least 40 years

B

Trees of **moderate quality** with an estimated remaining life expectancy of at least 20 years

C

Trees of **low quality** with an estimated remaining life expectancy of at least 10 years, or young trees with a stem diameter below 150mm

U

Unsuitable for retention

Those in such a condition that they cannot realistically be retained as living trees in the context of the current land use for longer than 10 years

Key to tree survey schedule: -

T	Tree	Age is classed as either: young; semi-mature, early-mature, mature or post-mature
G	Group	
W	Woodland	
H	Hedge	
		Life expectancy is classed as either: <10 years; 10+ years; 20+ years or 40+ years
RPA	Root protection area	The radial RPA is calculated as twelve times the stem diameter and represents the area where protection of the tree roots during development works is essential to the tree's future health and survival Where the RPA is not shown as circular on the tree survey plan, it may have been modified to take account of built structures such as buildings, roads or retaining walls
#	Estimated values	Measurements may have been estimated where the tree is inaccessible, such as if it is located on neighbouring land or if the stem is heavily covered in ivy Where trees have multiple stems, an average stem diameter may be given
≤ ≥ ≈		For groups of trees and hedges, measurements for the largest individual will be given or average measurements may be given where the individuals are approximately uniform

BS5837 Tree survey schedule

Site Rose Hill Farm, Whalley Old Road, Billington

Surveyor Jennie Keighley PhD MSc MArborA

Survey date 10 February 2026

Client Damian Hanson

Conditions Overcast, gentle breeze

Job no. LTC336

ID no.	Species Latin name	Stem diameter (mm)	Age	Height (m)#	Crown spread (m)	Crown clearance (m)	Structural condition Physiological condition	Life expectancy (years)	Radial RPA (m)	BS5837 category	General observations
T1	Purple Norway maple <i>Acer platanoides</i> Crimson King	520	Mature	12	N 5 E 5 S 5 W 5	2	Good Good	20+	6.2	B	Crown previously lifted; pruning wounds partially to fully occluded
T2	Sycamore <i>Acer pseudoplatanus</i>	300 #	Early-mature	9	N 4 E 4 S 4 W 4	1.75	Good Good	40+	3.6	B	- Growing beyond boundary stock fence and therefore evidently under neighbouring Highways Authority ownership - Single better quality tree growing within C-category group G4 - Light ivy cover growing up stem
T3	European beech <i>Fagus sylvatica</i>	1250	Mature	14	N 7 E 7 S 7 W 7	1.5	Moderate Moderate/Good	20+	15	A	- Veteran tree - Codominant stem removed in the past at a height of 1.5m - Stem diameter only refers to remaining stem, measured at a height of 1.75m - Approximately 12no. young to mature brackets of white rot decay fungus <i>Ganoderma australe</i> growing around full circumference of tree from base to a height of 1.25m (max. bracket width 700mm) - Large raised buttress roots on northern side - Flaking bark on remnants of removed stem - Several visible knotholes of varying sizes - Frequent deadwood on southern side of crown to a diameter of 100mm and length of 1m - Stem evidently failed at apex

BS5837 Tree survey schedule

Site Rose Hill Farm, Whalley Old Road, Billington

Surveyor Jennie Keighley PhD MSc MArborA

Survey date 10 February 2026

Client Damian Hanson

Conditions Overcast, gentle breeze

Job no. LTC336

ID no.	Species Latin name	Stem diameter (mm)	Age	Height (m)#	Crown spread (m)	Crown clearance (m)	Structural condition Physiological condition	Life expectancy (years)	Radial RPA (m)	BS5837 category	General observations
T4	Himalayan birch <i>Betula utilis</i>	230	Early-mature	10	N 3.5 E 3.5 S 3.5 W 3.5	1.5	Good Good	20+	2.8	C	- Ornamental tree within garden - No significant visible defects
G1	English oak Common ash Holly Hawthorn Rowan Sycamore Silver birch Hazel Field maple Black alder <i>Quercus robur</i> <i>Fraxinus excelsior</i> <i>Ilex aquifolium</i> <i>Crataegus monogyna</i> <i>Sorbus aucuparia</i> <i>Acer pseudoplatanus</i> <i>Betula pendula</i> <i>Corylus avellana</i> <i>Acer campestre</i> <i>Alnus glutinosa</i>	≤ 800 #	Young to mature	≤ 20	N ≤ 7 E ≤ 7 S ≤ 7 W ≤ 7	≥ 0	Poor to Good Dead to Good	40+	≤ 9.6	B	- Group of trees growing predominantly beyond boundary stock fence and therefore evidently under neighbouring ownership - Some of ash crowns exhibiting very early signs of infection with ash dieback disease - Large oak by site entrance has lost a large codominant leader in the past

BS5837 Tree survey schedule

Site Rose Hill Farm, Whalley Old Road, Billington

Surveyor Jennie Keighley PhD MSc MArborA

Survey date 10 February 2026

Client Damian Hanson

Conditions Overcast, gentle breeze

Job no. LTC336

ID no.	Species Latin name	Stem diameter (mm)	Age	Height (m)#	Crown spread (m)	Crown clearance (m)	Structural condition Physiological condition	Life expectancy (years)	Radial RPA (m)	BS5837 category	General observations
G2	3no. hawthorn 2no. holly <i>Crataegus monogyna</i> <i>Ilex aquifolium</i>	≤ 5x100 #	Mature	≤ 7	N ≤ 3 E ≤ 3 S ≤ 3 W ≤ 3	≥ 0	Good Good	20+	≤ 2.7	C	Scattered linear group of small trees growing in raised verge on southern side of driveway
G3	Gorse <i>Ulex europaeus</i>	≈ 100	Mature	≤ 3.5	N 2.5 E 2.5 S 2.5 W 2.5	0	Good Good	20+	1.2	C	Dense thickets at field edge
G4	Hawthorn Goat willow Common ash Sycamore English oak Holly European beech <i>Crataegus monogyna</i> <i>Salix caprea</i> <i>Fraxinus excelsior</i> <i>Acer pseudoplatanus</i> <i>Quercus robur</i> <i>Ilex aquifolium</i> <i>Fagus sylvatica</i>	≤ 250 #	Young to mature	≤ 9	N ≤ 6 E ≤ 6 S ≤ 6 W ≤ 6	≥ 0	Poor to Good Dead to Good	20+	≤ 3	C	- Grown-out hedge and young trees growing along road verge and atop old stone boundary wall - Growing beyond boundary stock fence and therefore evidently under neighbouring Highways Authority ownership - Historically laid - Ash crowns exhibiting signs of early to advanced infection with ash dieback disease - Some of ash dead - One sycamore moribund

BS5837 Tree survey schedule

Site Rose Hill Farm, Whalley Old Road, Billington

Surveyor Jennie Keighley PhD MSc MArborA

Survey date 10 February 2026

Client Damian Hanson

Conditions Overcast, gentle breeze

Job no. LTC336

ID no.	Species Latin name	Stem diameter (mm)	Age	Height (m)#	Crown spread (m)	Crown clearance (m)	Structural condition Physiological condition	Life expectancy (years)	Radial RPA (m)	BS5837 category	General observations
G5	English oak	≤ 500 #	Young to mature	≤ 18	N ≤ 8 E ≤ 8 S ≤ 8 W ≤ 8	≥ 0	Poor to Good	40+	≤ 6	B	- Group of trees growing predominantly beyond boundary stock fence and therefore evidently under neighbouring ownership - Ash crowns exhibiting signs of advanced infection with ash dieback disease - Single oak growing within site has a woodpecker nest hole at chest height
	Hazel										
	Holly										
	Black alder										
	Common ash										
	Rowan										
	European beech										
	Blackthorn										
	Hawthorn										
	Bird cherry										
	<i>Quercus robur</i>										
	<i>Corylus avellana</i>										
	<i>Ilex aquifolium</i>										
	<i>Alnus glutinosa</i>										
	<i>Fraxinus excelsior</i>										
	<i>Sorbus aucuparia</i>										
	<i>Fagus sylvatica</i>										
	<i>Prunus spinosa</i>										
	<i>Crataegus monogyna</i>										
	<i>Prunus padus</i>										
							Moribund to Good				

BS5837 Tree survey schedule

Site Rose Hill Farm, Whalley Old Road, Billington

Surveyor Jennie Keighley PhD MSc MArborA

Survey date 10 February 2026

Client Damian Hanson

Conditions Overcast, gentle breeze

Job no. LTC336

ID no.	Species Latin name	Stem diameter (mm)	Age	Height (m)#	Crown spread (m)	Crown clearance (m)	Structural condition Physiological condition	Life expectancy (years)	Radial RPA (m)	BS5837 category	General observations
G6	≈10no. holly 2no. hazel 1no. hawthorn <i>Ilex aquifolium</i> <i>Corylus avellana</i> <i>Crataegus monogyna</i>	≤ 250 #	Young to mature	≤ 8	N ≤ 4 E ≤ 4 S ≤ 4 W ≤ 4	≥ 0	Moderate to Good Moribund to Good	10+	≤ 3	C	- Clusters of small trees within north-western corner of field - Trees mostly multi-stemmed - Two of hollies moribund
H1	Hornbeam Hazel Hawthorn Holly Elder Sycamore European beech <i>Carpinus betulus</i> <i>Corylus avellana</i> <i>Crataegus monogyna</i> <i>Ilex aquifolium</i> <i>Sambucus nigra</i> <i>Acer pseudoplatanus</i> <i>Fagus sylvatica</i>	≈ 80	Mature	≤ 3	N ≤ 1 E ≤ 1 S ≤ 1 W ≤ 1	0	Good Good	40+	1	C	- Garden boundary hedge - Managed at varying heights - Predominantly hornbeam and hazel where surrounding lawn
